


EXISTING CONDITIONS

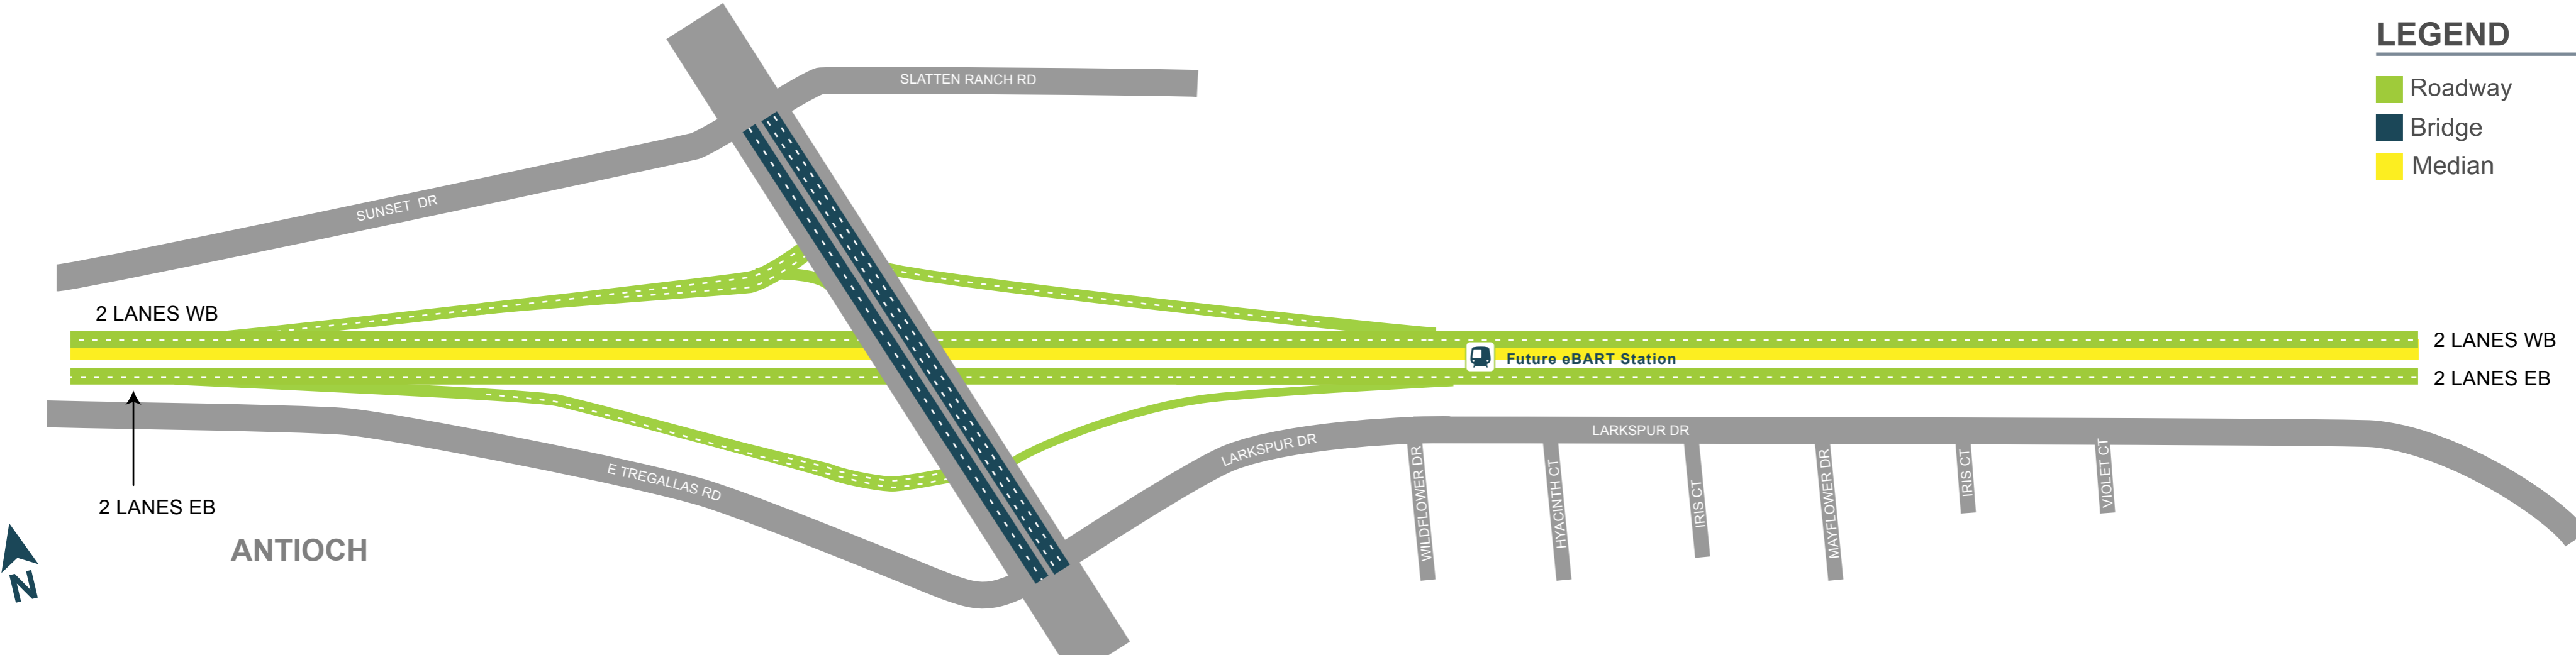


LANE SHIFT CONSTRUCTION:

Shift eastbound ramp south. Build temporary pavement for traffic. Remove median. Construct center bridge foundations.

1

LEGEND

- Roadway
- Construction
- Median
- Bridge

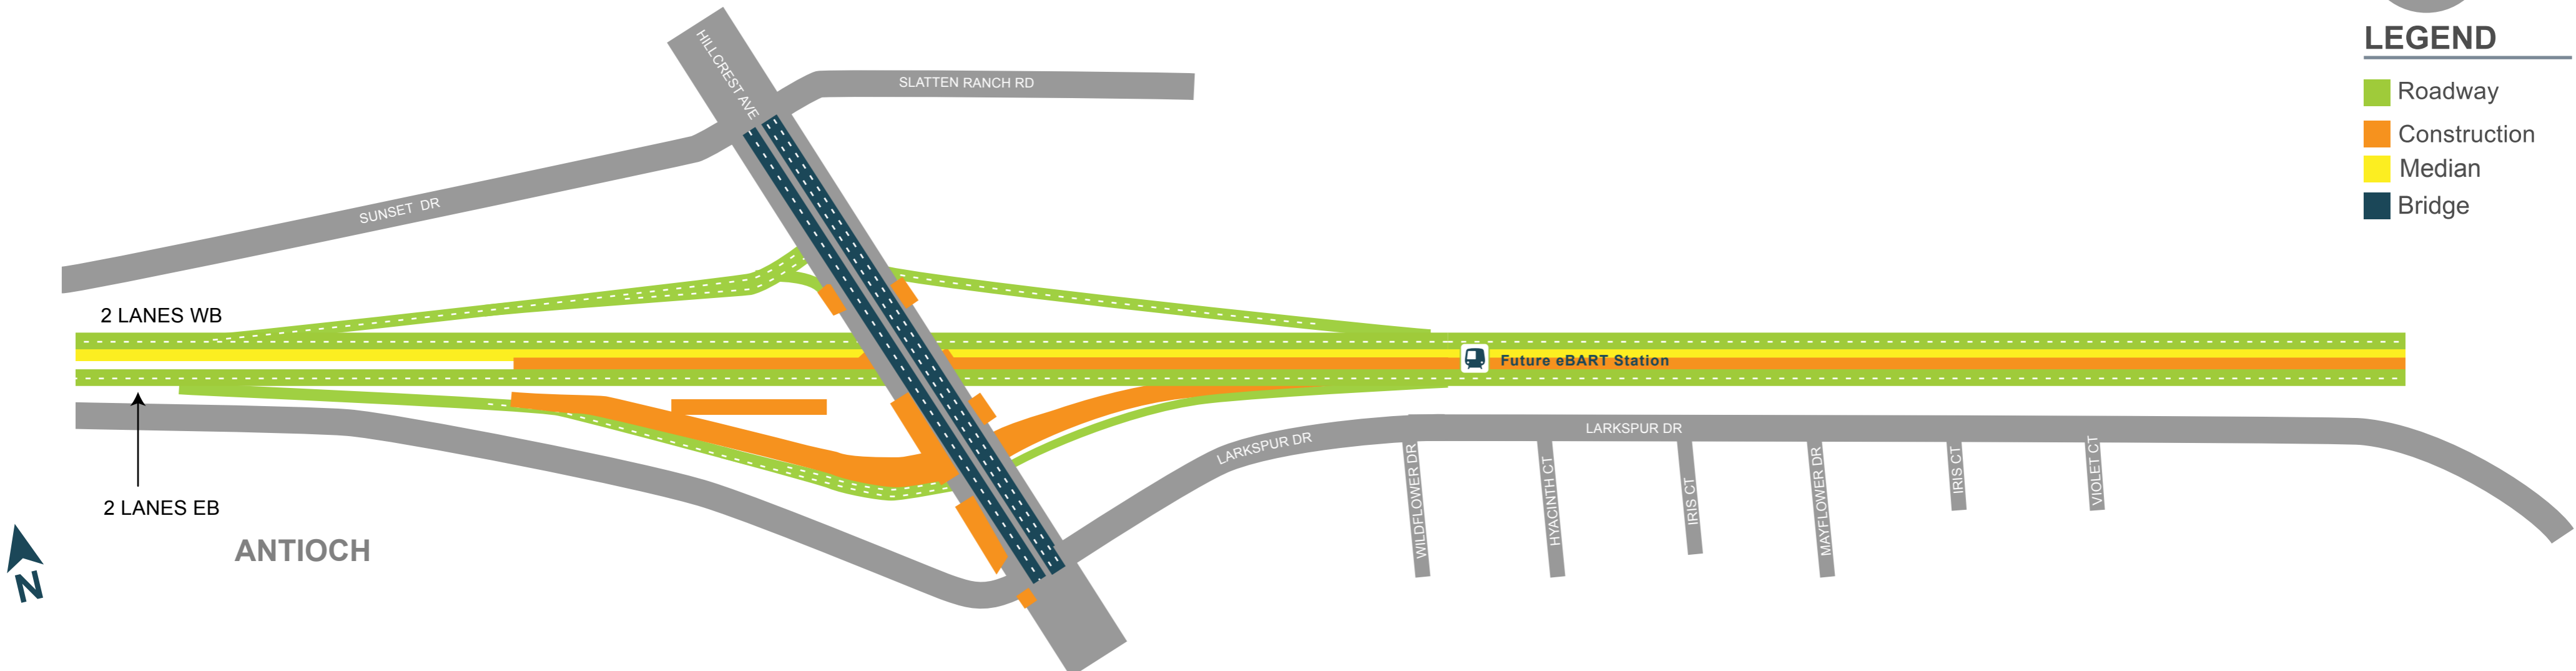


LANE SHIFT CONSTRUCTION:

Shift eastbound traffic north onto the temporary pavement. Shift eastbound exit ramp north onto temporary pavement. Construct retaining walls for new Hillcrest Ave bridge. Construct temporary and permanent pavement for traffic.

2

LEGEND

- Roadway
- Construction
- Median
- Bridge

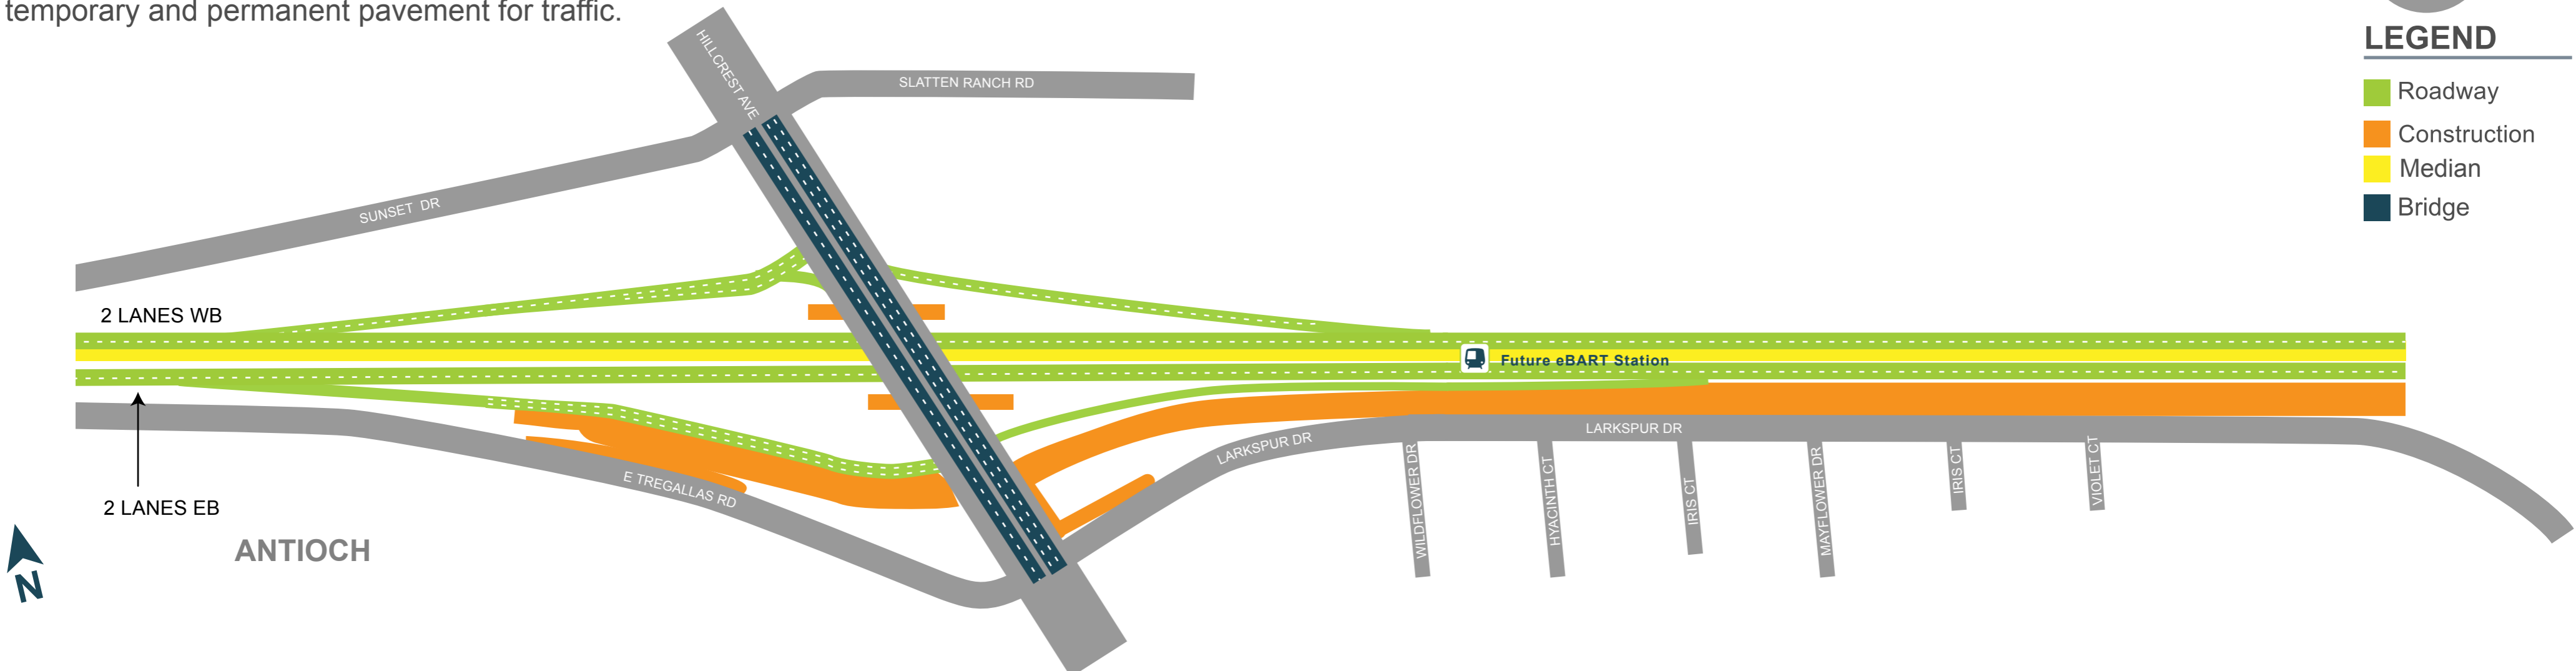


LANE SHIFT CONSTRUCTION:

Shift eastbound traffic north slightly. Shift eastbound exit ramp south onto new pavement. Shift eastbound on-ramp south onto new pavement. Construct temporary pavement and a portion of permanent pavement of eastbound Highway 4.

3

LEGEND

- Roadway
- Construction
- Median
- Bridge

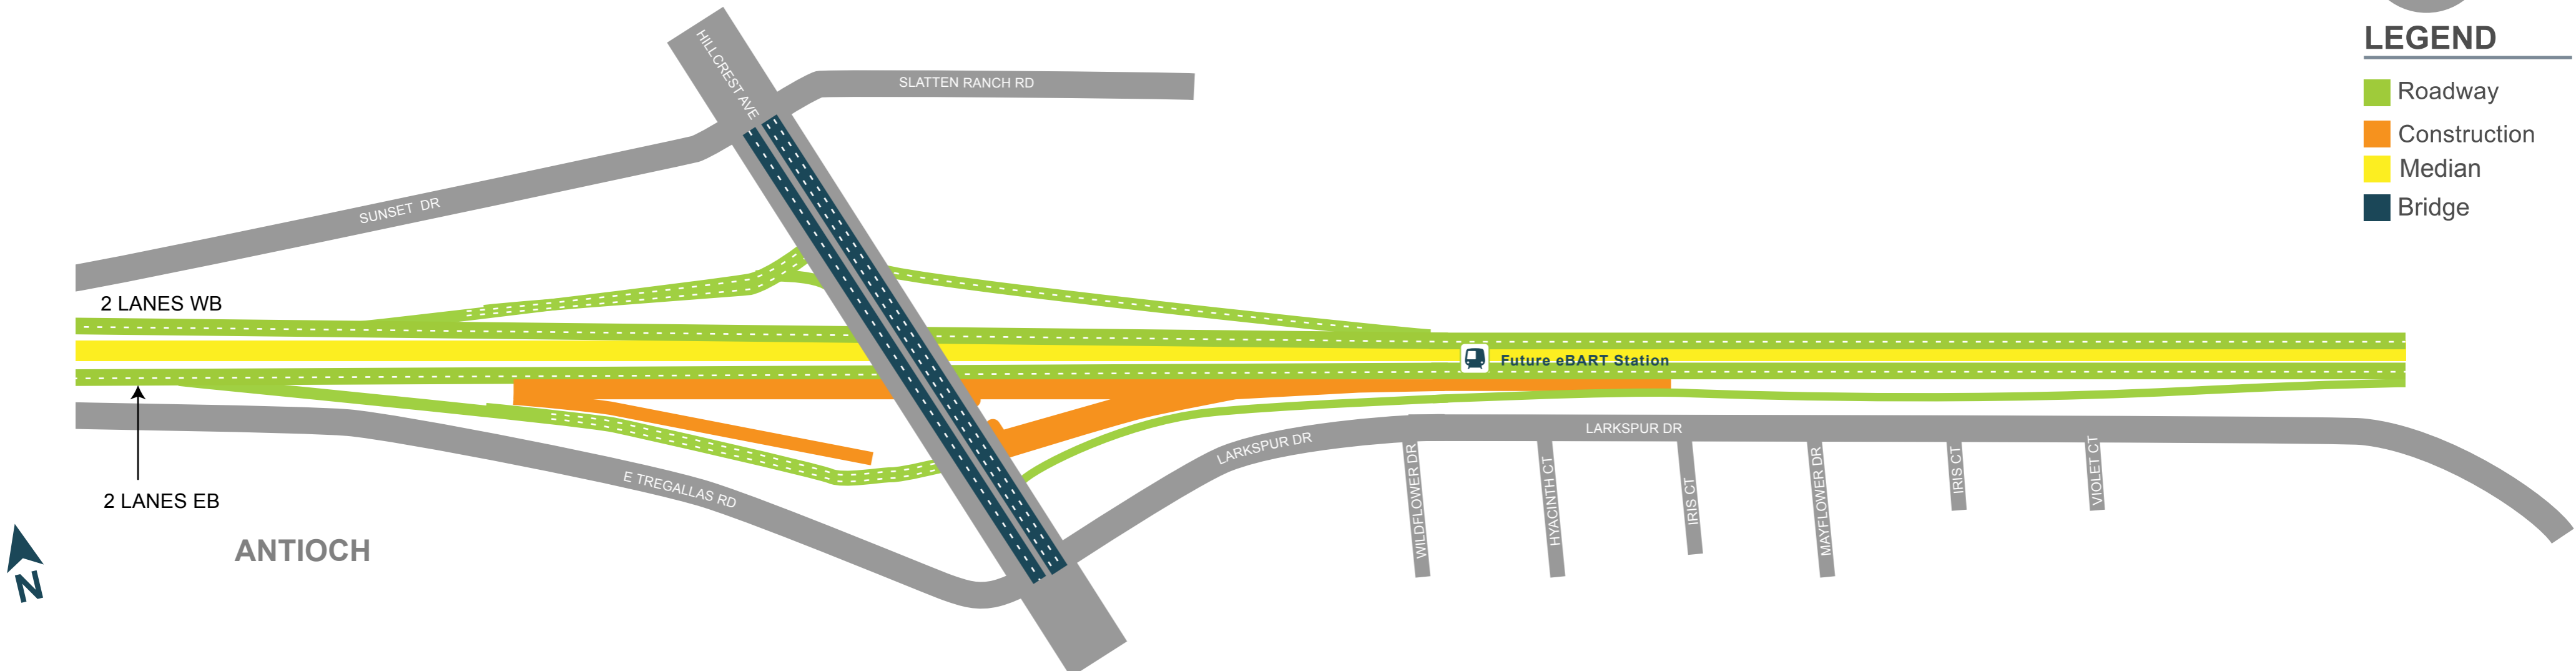

ANTIOCH


LANE SHIFT CONSTRUCTION:

Shift eastbound traffic south onto temporary pavement. Shift eastbound exit and entrance ramps north onto new pavement. Construct temp and permanent pavement. Construct temporary pavement for median crossover.

4

LEGEND

- Roadway
- Construction
- Median
- Bridge

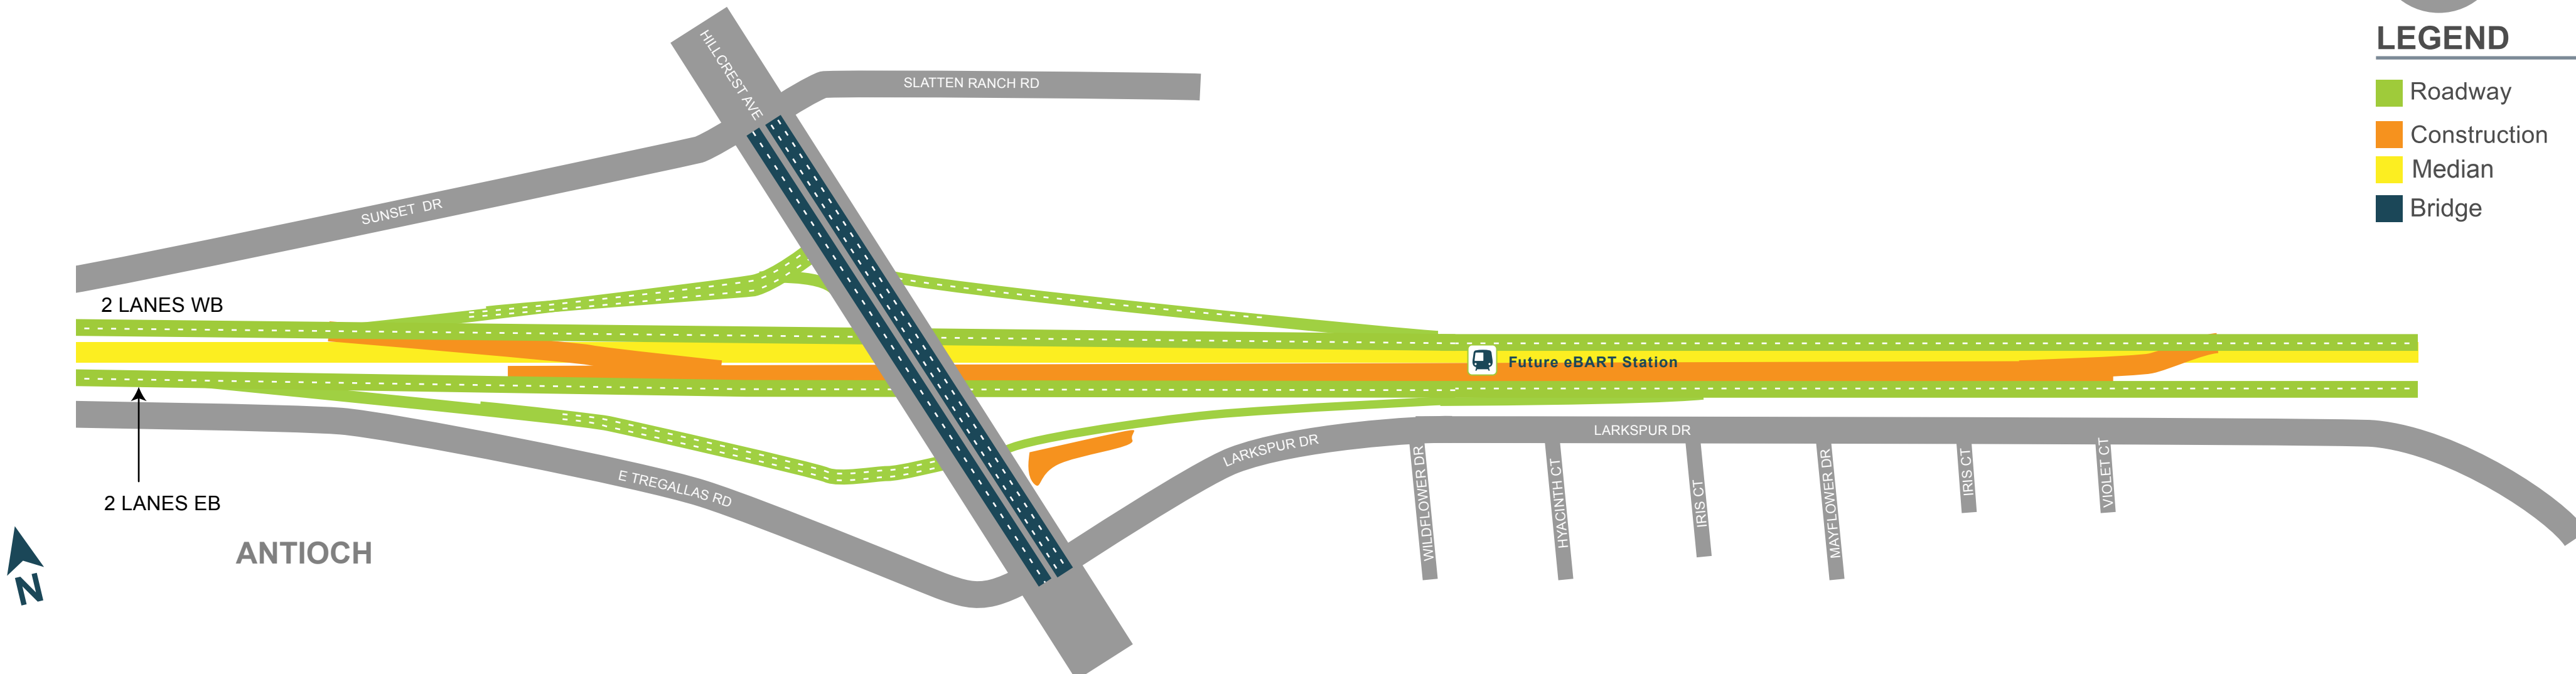


LANE SHIFT CONSTRUCTION:

Shift westbound traffic along the cross median detour onto eastbound Highway 4. Construct temporary pavement and new Hillcrest Bridge.

5

LEGEND

- Roadway
- Construction
- Median
- Bridge

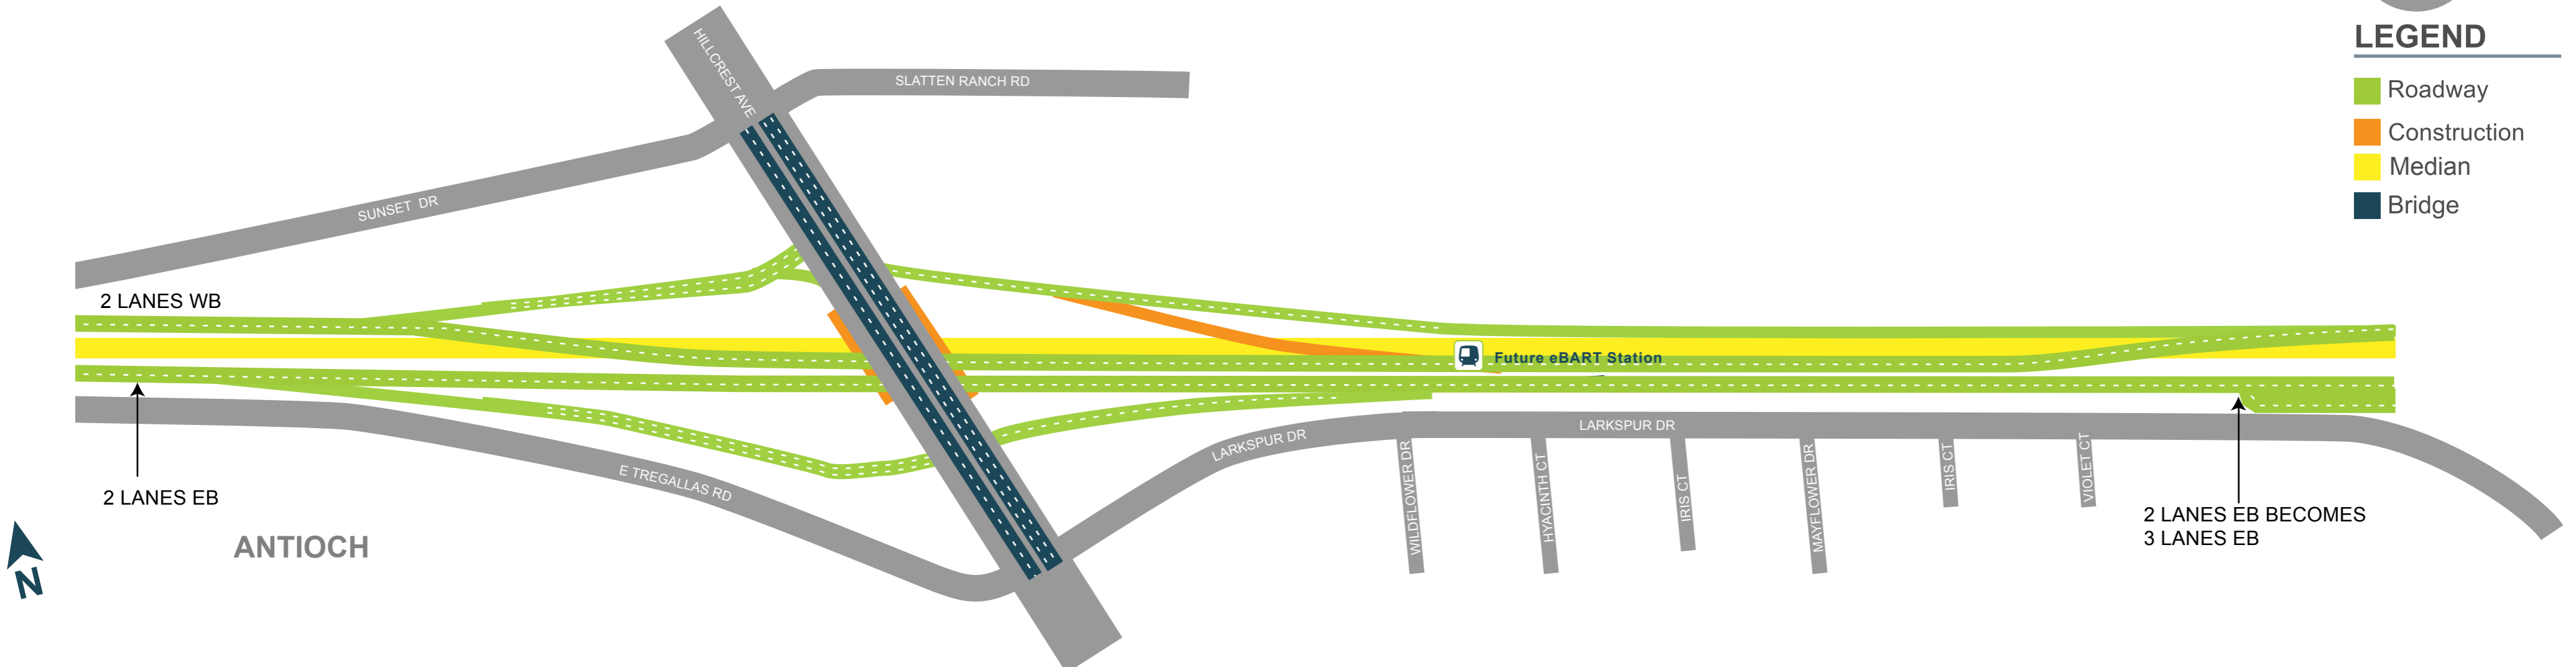


LANE SHIFT CONSTRUCTION:

Shift westbound exit south onto temporary pavement. Begin construction of Hillcrest median. Construct temporary and permanent pavement. Continue to construct Hillcrest bridge. Construct eBART station entry house, eBART pedestrian overcrossing, and eBART station platform. Construct new westbound off-ramp and Slatten Ranch Road.

6

LEGEND

- Roadway
- Construction
- Median
- Bridge

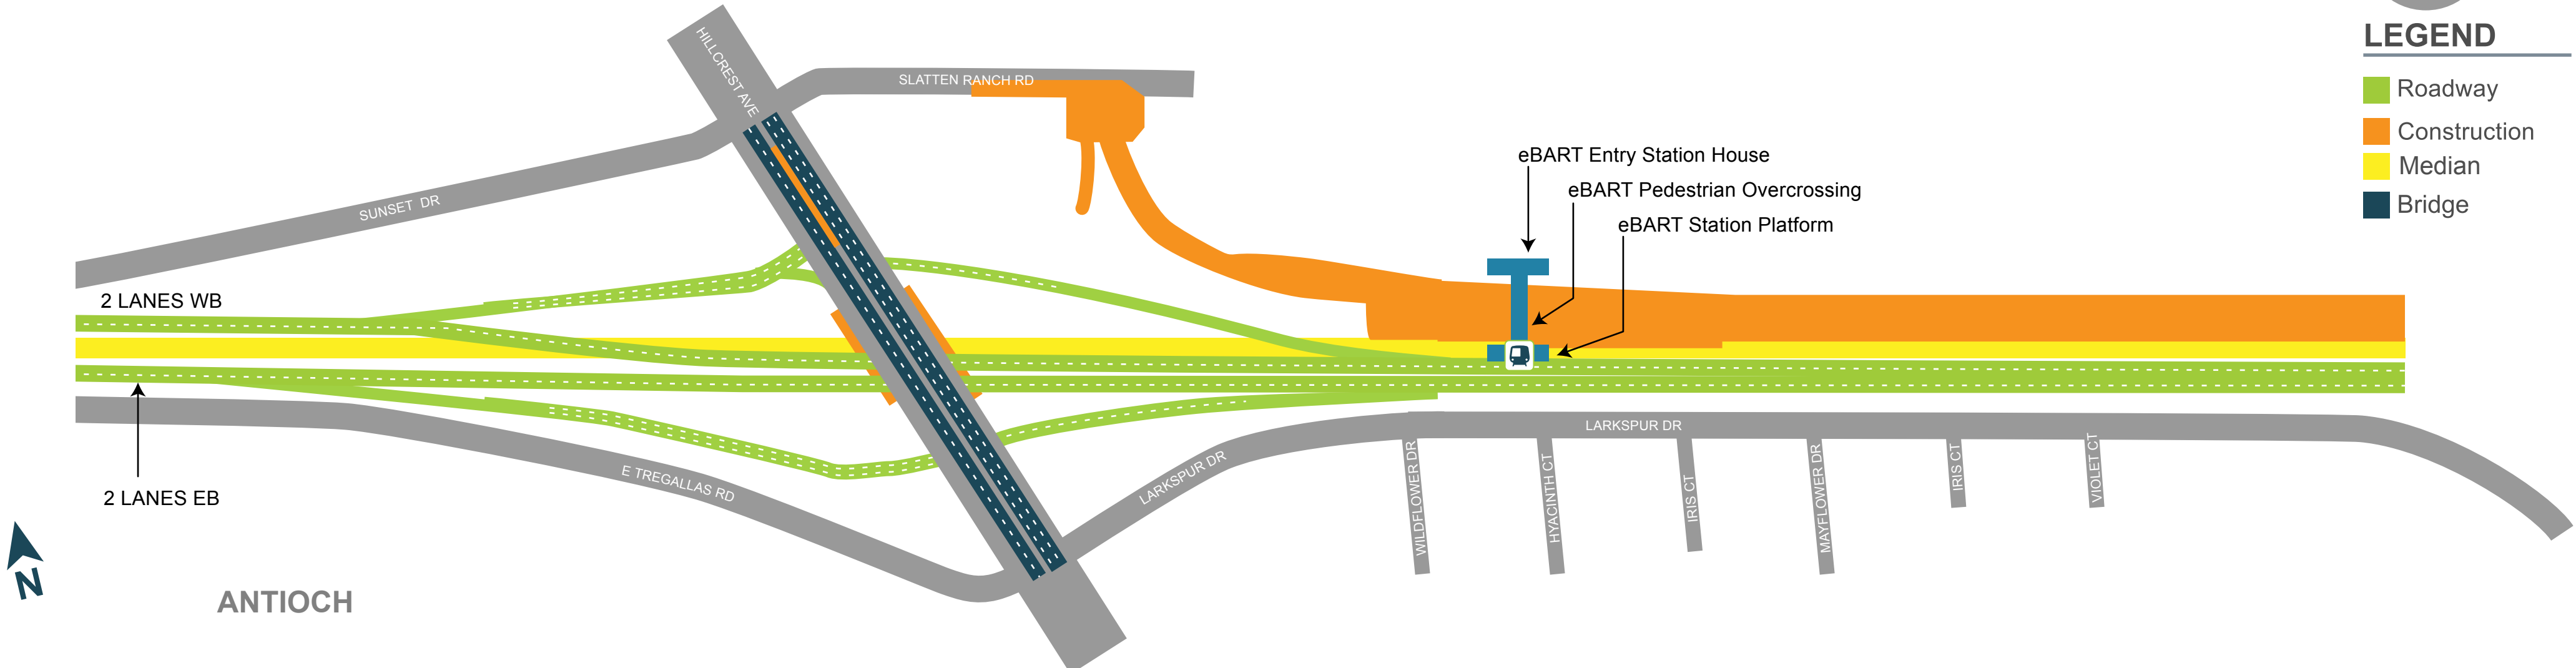


LANE SHIFT CONSTRUCTION:

Shift westbound exit ramp north onto new pavement. Construct temporary and permanent pavement. Shift westbound off-ramp north onto new alignment to Slatten Ranch Road. Construct new westbound loop on-ramp from Slatten Ranch Road.

7

LEGEND

- Roadway
- Construction
- Median
- Bridge

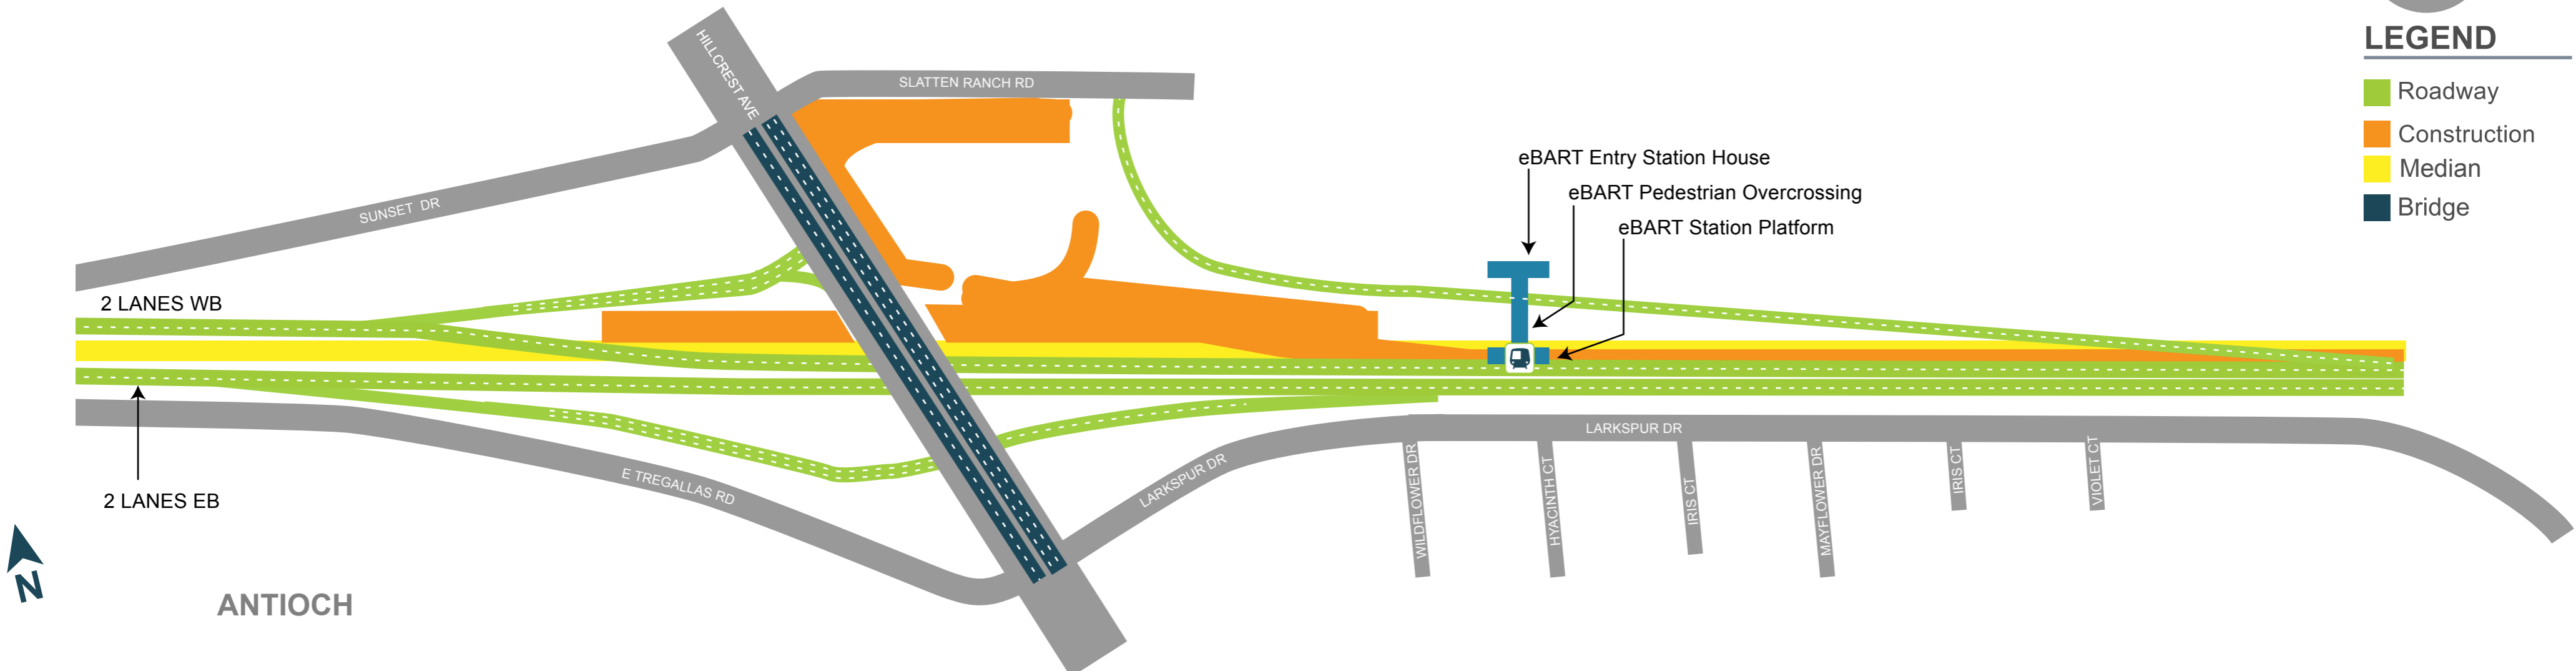


LANE SHIFT CONSTRUCTION:

Shift westbound traffic north onto new pavement. Shift Hillcrest traffic to have 2 lanes northbound and 3 lanes southbound. Shift west bound on-ramp east to new pavement. Construct new and temporary pavement. Construct westbound diagonal on-ramp from Hillcrest Avenue.

8

LEGEND

- Roadway
- Construction
- Median
- Bridge

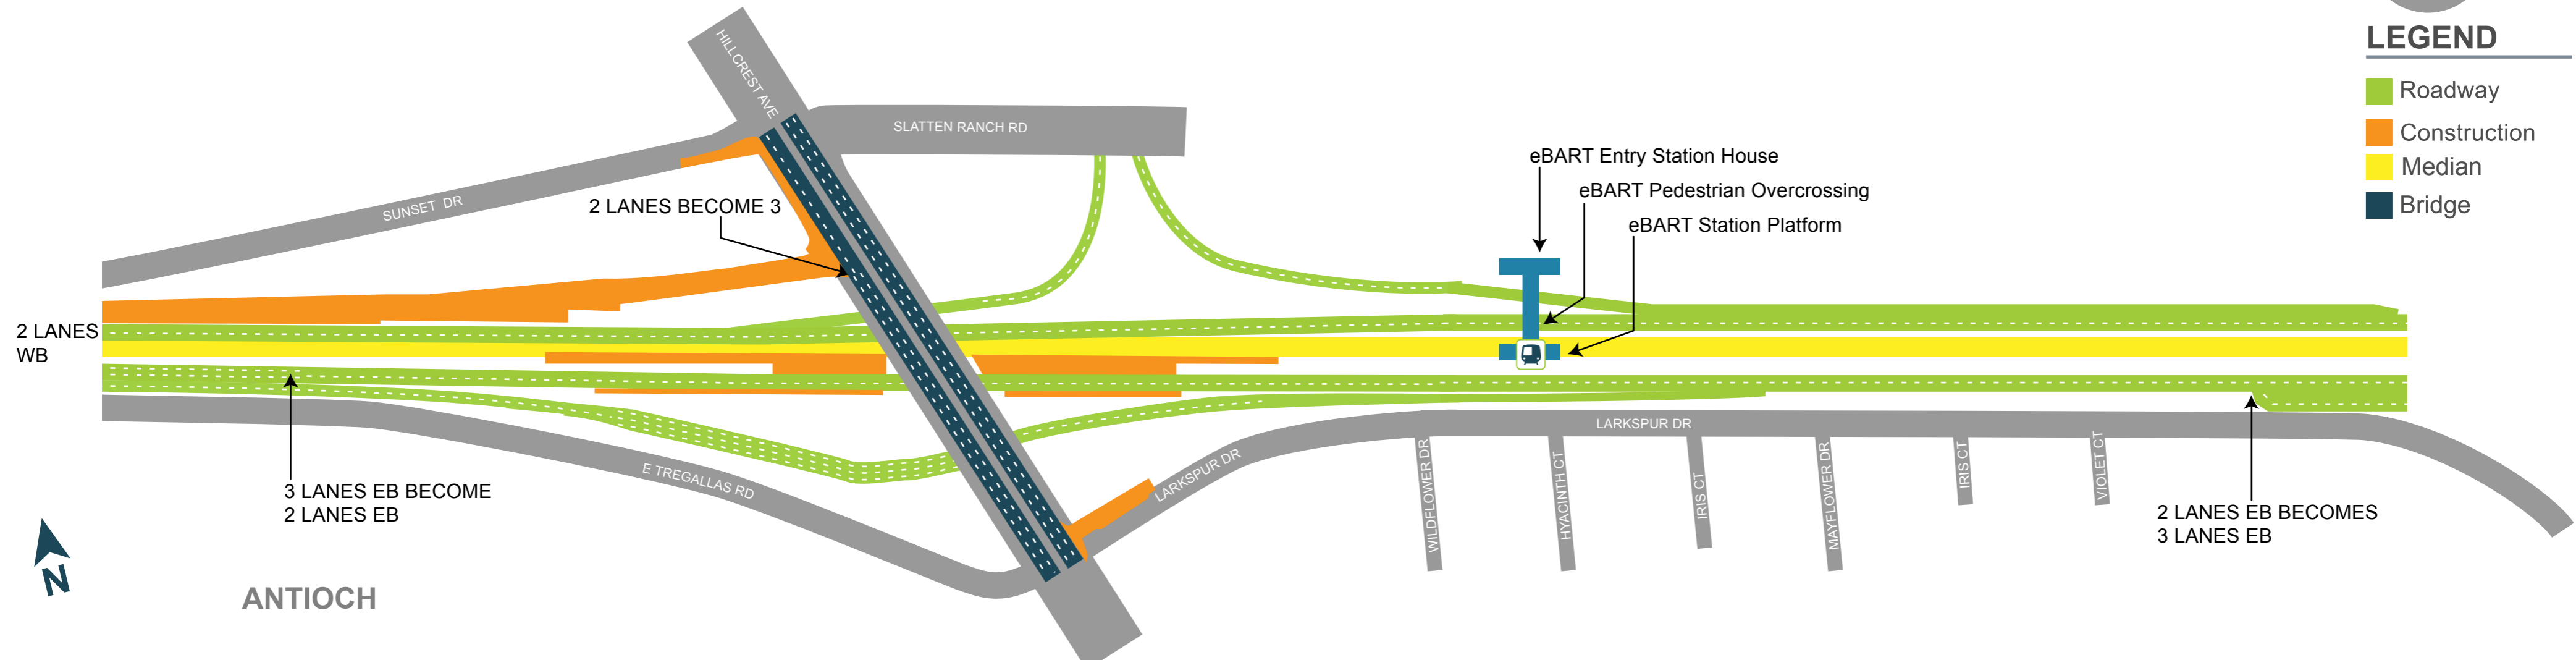

2 LANES WB

2 LANES BECOME 3

3 LANES EB BECOME 2 LANES EB

2 LANES EB BECOMES 3 LANES EB

ANTIOCH




LANE SHIFT CONSTRUCTION:

Shift eastbound traffic north onto temporary pavement. Construct new pavement.

9

LEGEND

- Roadway
- Construction
- Median
- Bridge

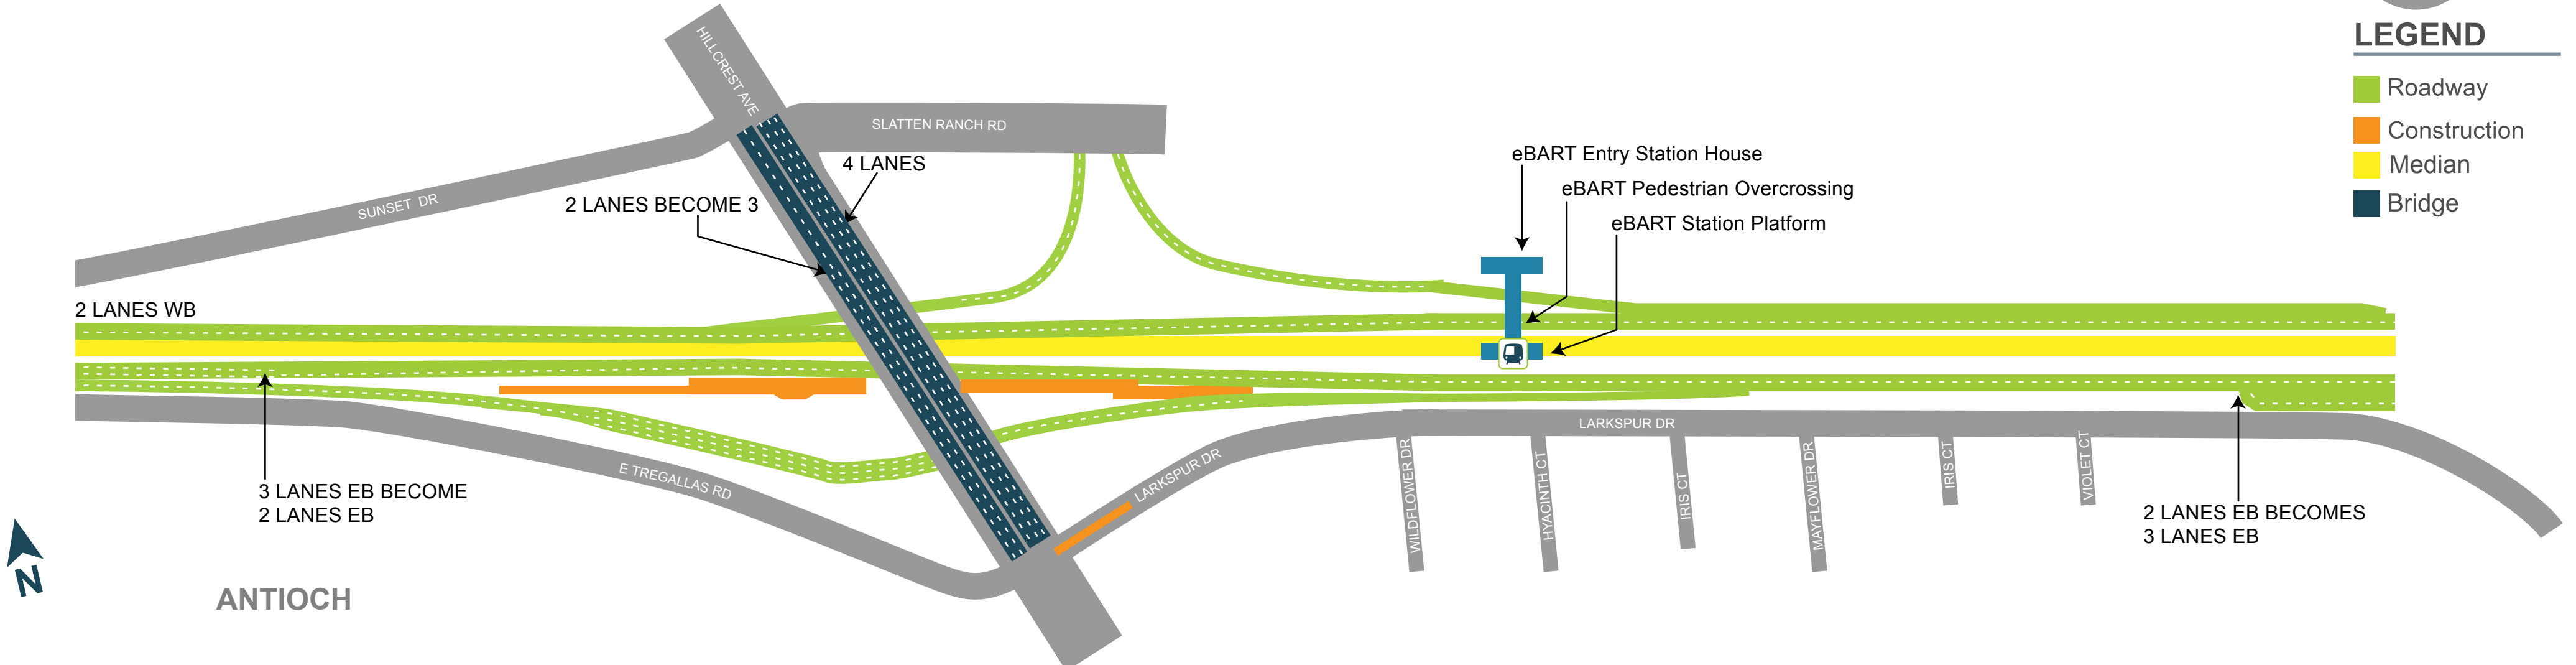


LANE SHIFT CONSTRUCTION:

Shift eastbound traffic north slightly. Construct new pavement.

10

LEGEND

- Roadway
- Construction
- Median
- Bridge

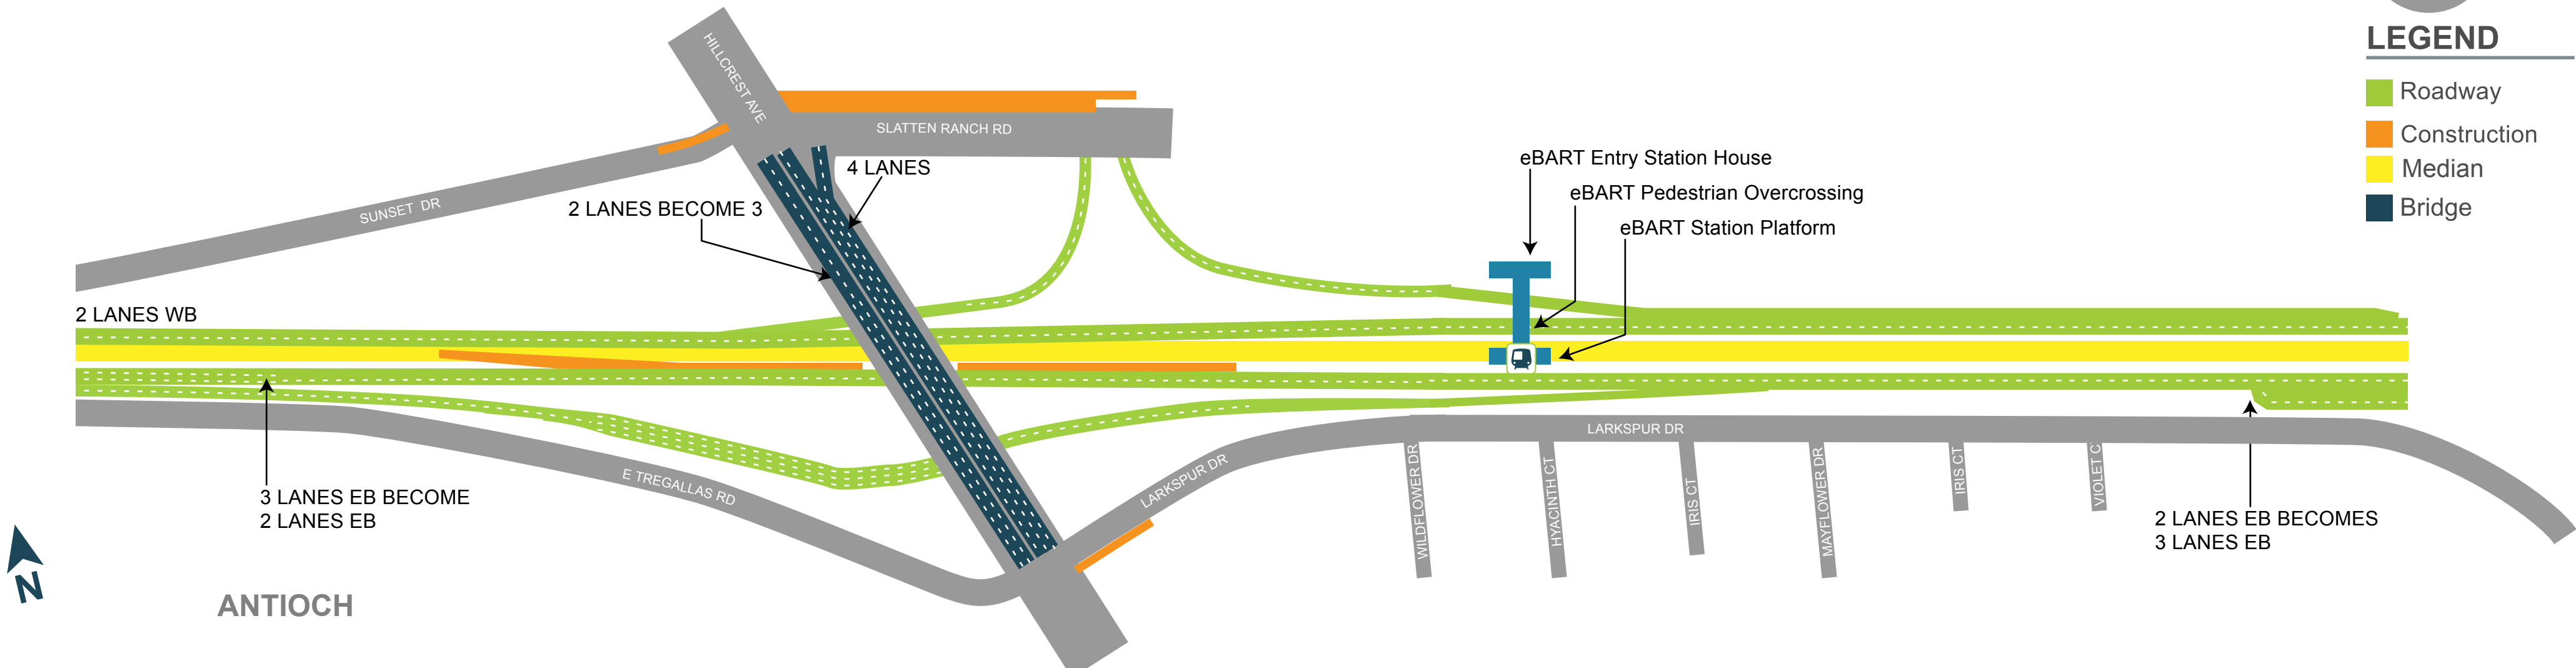


LANE SHIFT CONSTRUCTION:

Shift eastbound traffic north to final alignment. Construct new pavement.

11

LEGEND

- Roadway
- Construction
- Median
- Bridge

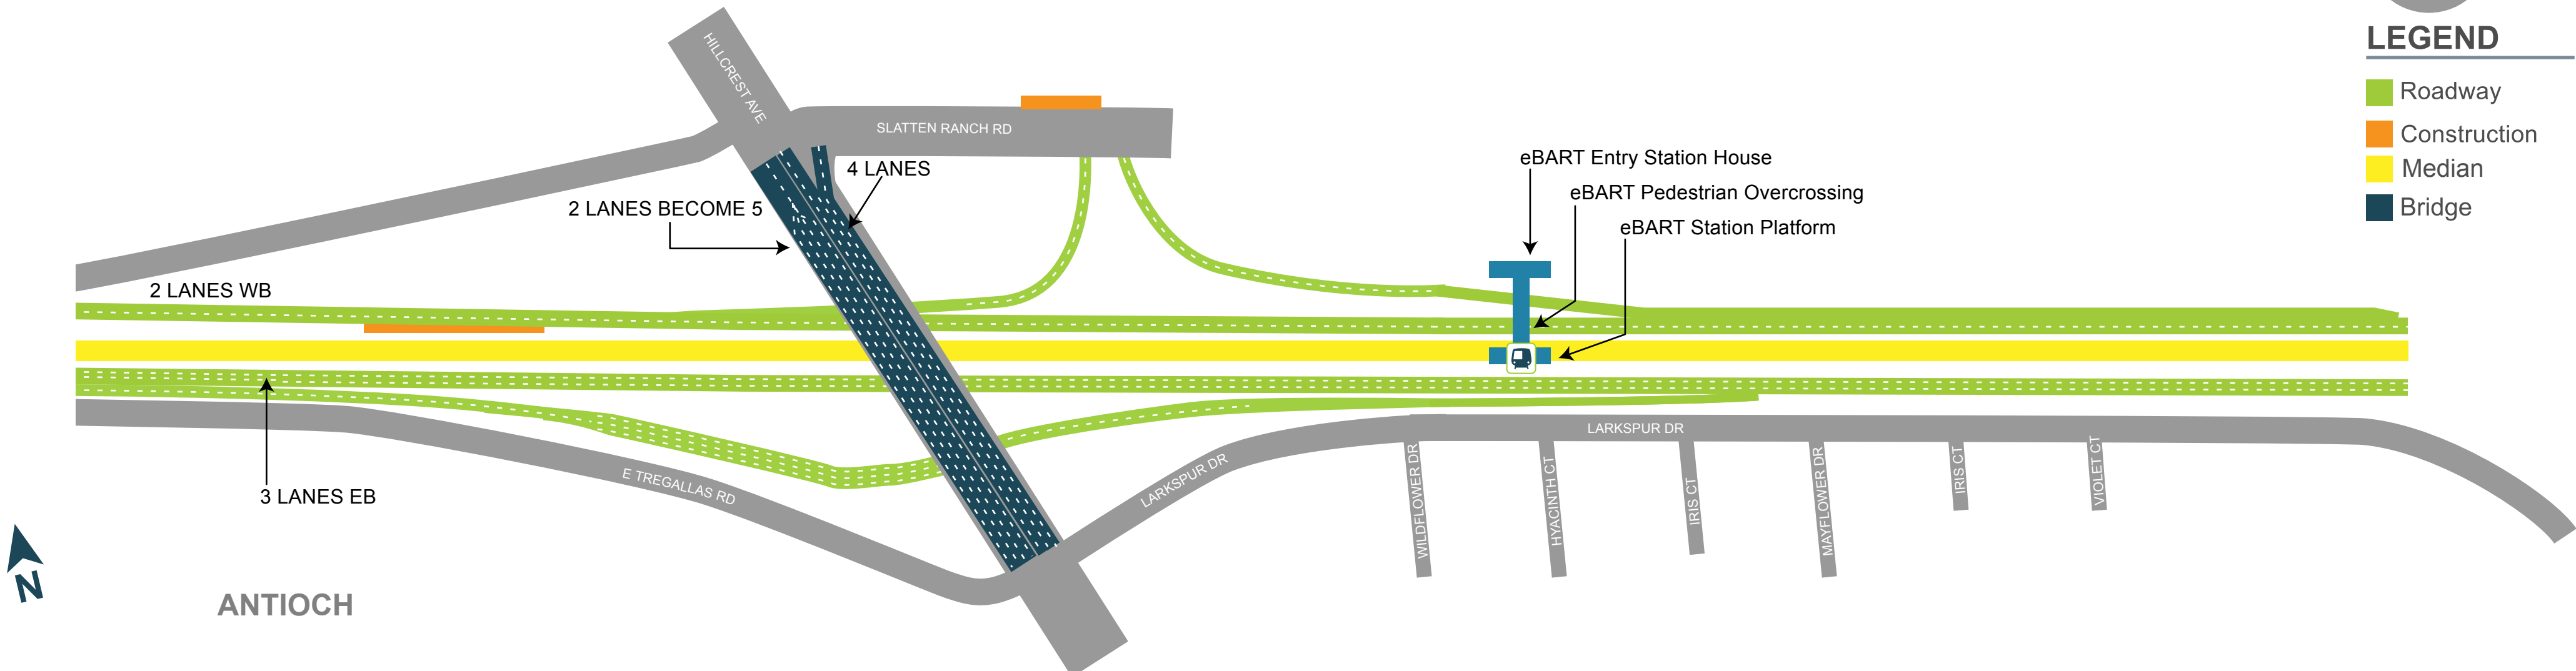


LANE SHIFT CONSTRUCTION:

Shift westbound traffic south onto new pavement. Construct new pavement.

12

LEGEND

- Roadway
- Construction
- Median
- Bridge

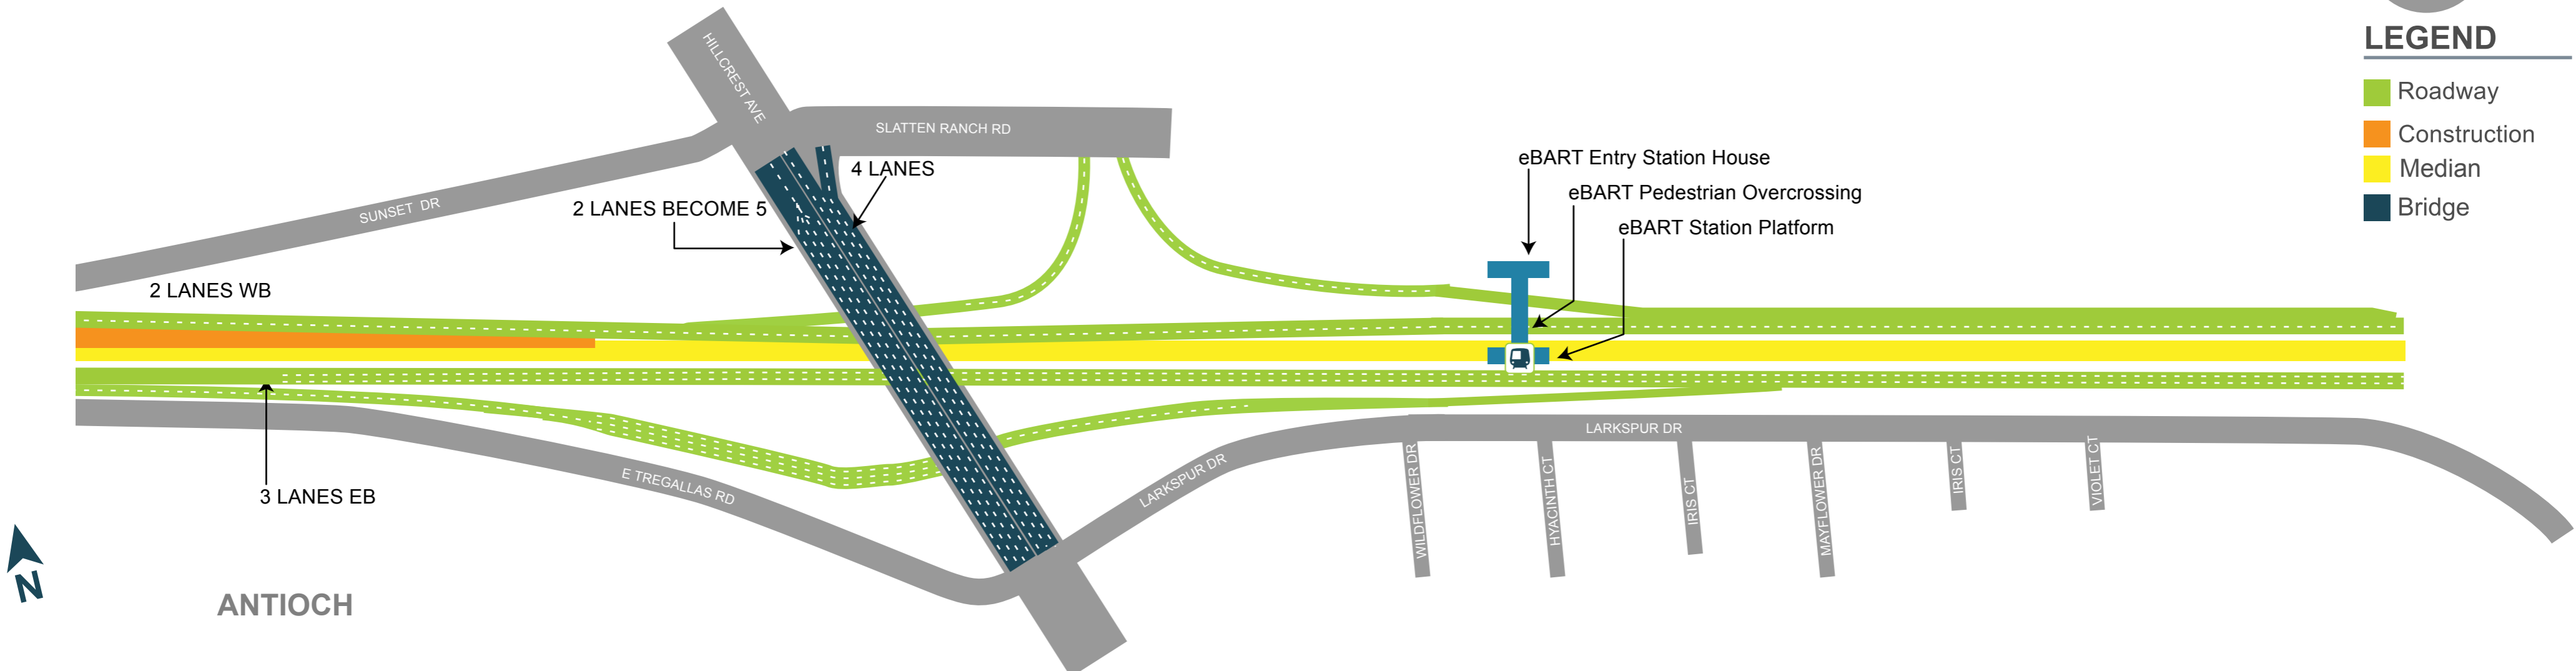

FINAL ALIGNMENT

